



① PHASE 1

- BUILD ECC

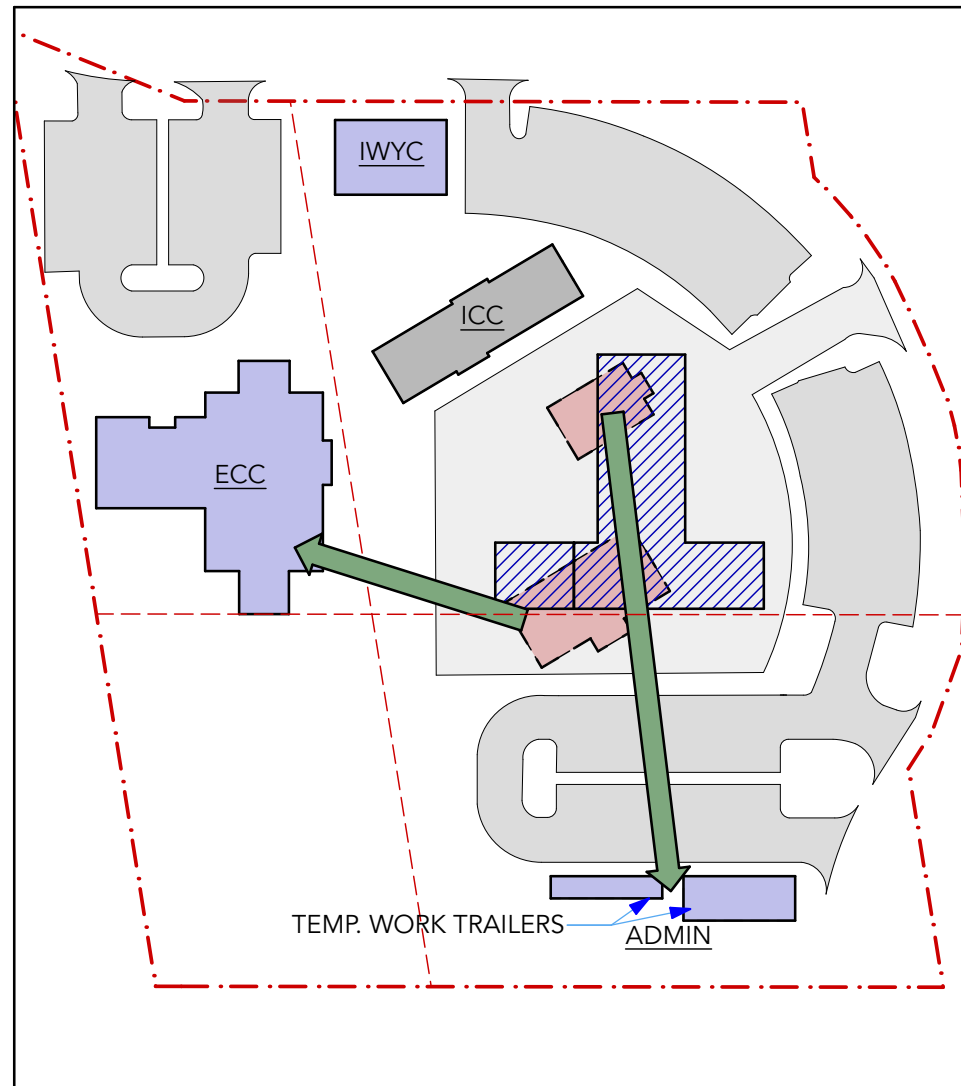


② PHASE 2

- MOVE ECC TO NEW BUILDING
- MOVE ADMIN TO TEMPORARY WORK TRAILERS
- BUILD NEW PARKING AND DELINEATE CONSTRUCTION ZONE
- DEMO ADMIN AND ECC BUILDINGS
- BUILD NEW COMMUNITY SERVICES BUILDING

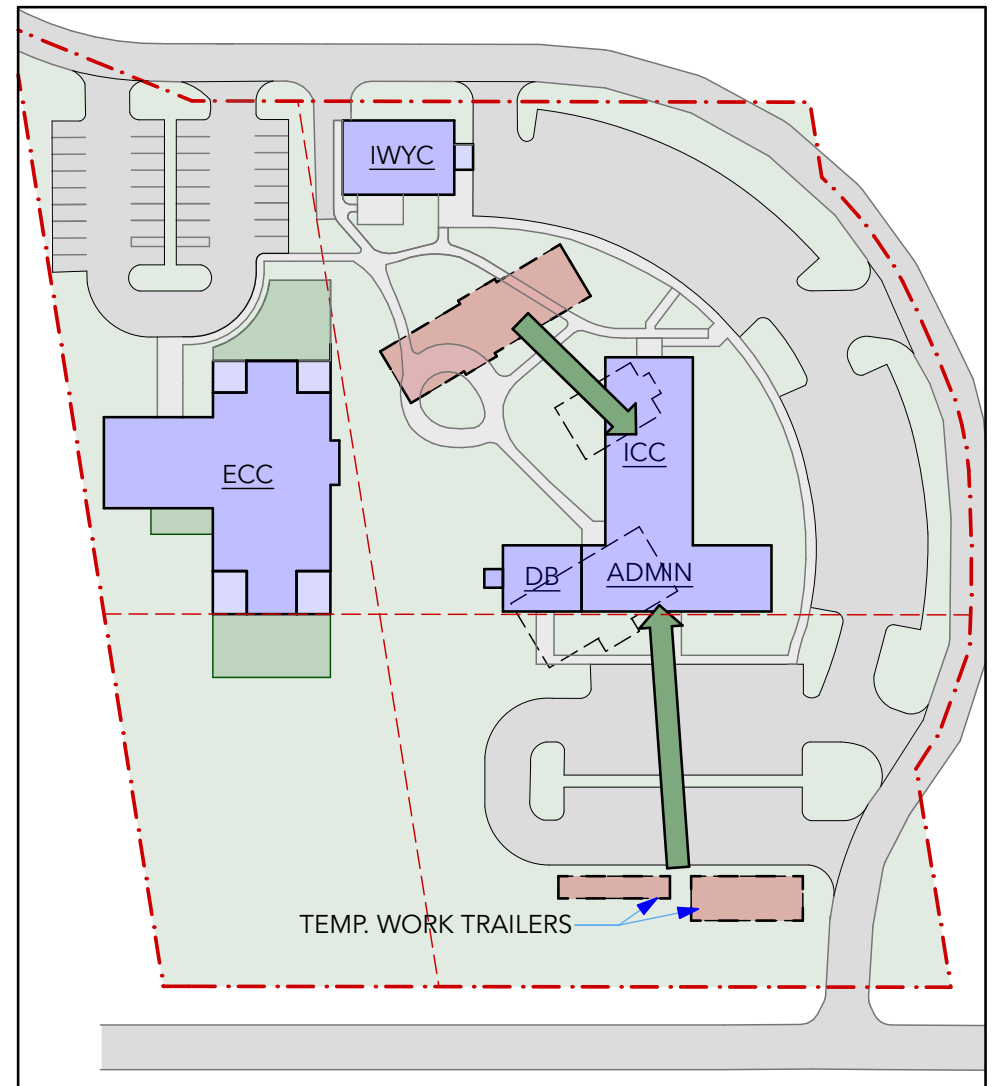

③ PHASE 3

- MOVE ICC, ADMIN, AND DAYBREAK (CURRENTLY OFF-SITE) TO NEW COMMUNITY SERVICES BUILDING
- DEMO ICC AND REMOVE WORK TRAILERS
- FINISH PARKING AND LANDSCAPE



Phasing Plans
